Overview

Sprint #6, 3/12 – 3/26 (3 Class Sessions)

Team Members: Will Paxton (Scrum Master), Daniel Kefene (Product Owner), Nick Trahan, Mason Moore, Tyler Stephens

GitHub Link: https://github.com/willpaxton/MartRacers

Sprint Goals

This sprint was primarily focused on getting back on track after the break, as well as doing a few odd research related tasks to cover some of the later features to be integrated into the project. We overall wanted to continue development on the prototype and getting preparations made for integrating future features (like saving gameplay data and users).

User Stories Worked on this Sprint:

- "As a user, I want to use my mobile camera to scan a barcode."
- "As a user, I want the game to be able to determine who won the race."
- "As a user, I want the game to keep track of various statistics, such as my fastest times."

Sprint Planning & PBIs

For this sprint, we wanted to begin on merging our front and backend prototypes showcased during the midterm presentation together. Also, with this sprint being placed during and after spring break, we wanted to pursue tasks more open, planning style steps versus standard development, since we may not be the most efficient at those tasks as of this time.

Total Time Spent in Hours

There were around twenty-five man-hours available for this sprint between all members. This time was split between scrum meetings, tasks, and any additional work.

Tasks Performed

Task 1: Merge Front and Back End

Task Owner: Tyler Stephens, Daniel Kefene

Task Status: In-Progress

Planned Task Duration: 10 Hours

Actual Task Duration: 12 Hours

Description: Tyler and Daniel worked on merging the two parts of the prototype into one main product. This has proved to be a much more complicated process than originally thought, with this task potentially taking multiple sprints to fully complete. This sprint was focused on the two of them coming up with a plan to merge the two halves, along with some changes in the GitHub to make this process easier.

Task 2: Implement Automated Testing

Task Owners: Nick Trahan, Will Paxton

Task Status: In-Progress

Planned Task Duration: 5 Hours

Actual Task Duration: 7 Hours

Task Description: Nick began working with Selenium to understand how it works to integrate it with our project. His work this week was mostly spent learning how to use the framework, which will be integrated into the project in a future sprint. Will supported Nick in this sprint in helping him learn Selenium.

Task 3: Database Integration

Task Owners: Mason Moore

Task Status: In review/Completed

Planned Task Duration: 4 Hours

Actual Task Duration: 3 Hours

Task Description: Mason helped to bridge the gap between the front and back ends by setting up the database to work on the combined product, making integration of the two halves easier.

Task 4: Integrating User Pipelines

Task Owners: Mason Moore

Task Status: In-Progress

Planned Task Duration: 8 Hours

Actual Task Duration: 4 Hours (So Far)

Task Description: Mason began to modify the database and code in order to accept logged in users to the application. This also consisted of research of how to best handle logins on the website if the team had enough time to implement them in a later sprint.

Roadblocks

There were no major roadblocks with any tasks this sprint.

Sprint Review

Overall, we knew going into this sprint that we may not meet all the goals that we had set early on with our tasks, and that was okay. Due to Spring Break, we expected to take more time to get back up to speed on the project and mostly wanted to use this sprint to get back in the flow of things, which fortunately was met by the end of the sprint. There have also been good foundations made for future development of the project on nearly all fronts.

Sprint Retrospective

We did not get as much done as we wished, however, we did expect it with having a break in between the last time we had worked on the project, as well as having less man-hours to put towards the project. Knowing this could be the case early on, we chose smaller tasks that mostly required research to help set up for the sprints in the future where we would be able to contribute more time to the project.

Scrum Meetings

Our first scrum meeting after break was ultimately started by everyone saying that they had not worked on the project over the break. Our second scrum meeting on Thursday proved more eventful, as Mason had investigated ORMs as an alternative to databases, Nick had looked further into Selenium testing, and Daniel and Tyler worked on features for the prototype.

Scrum/Kanban Board

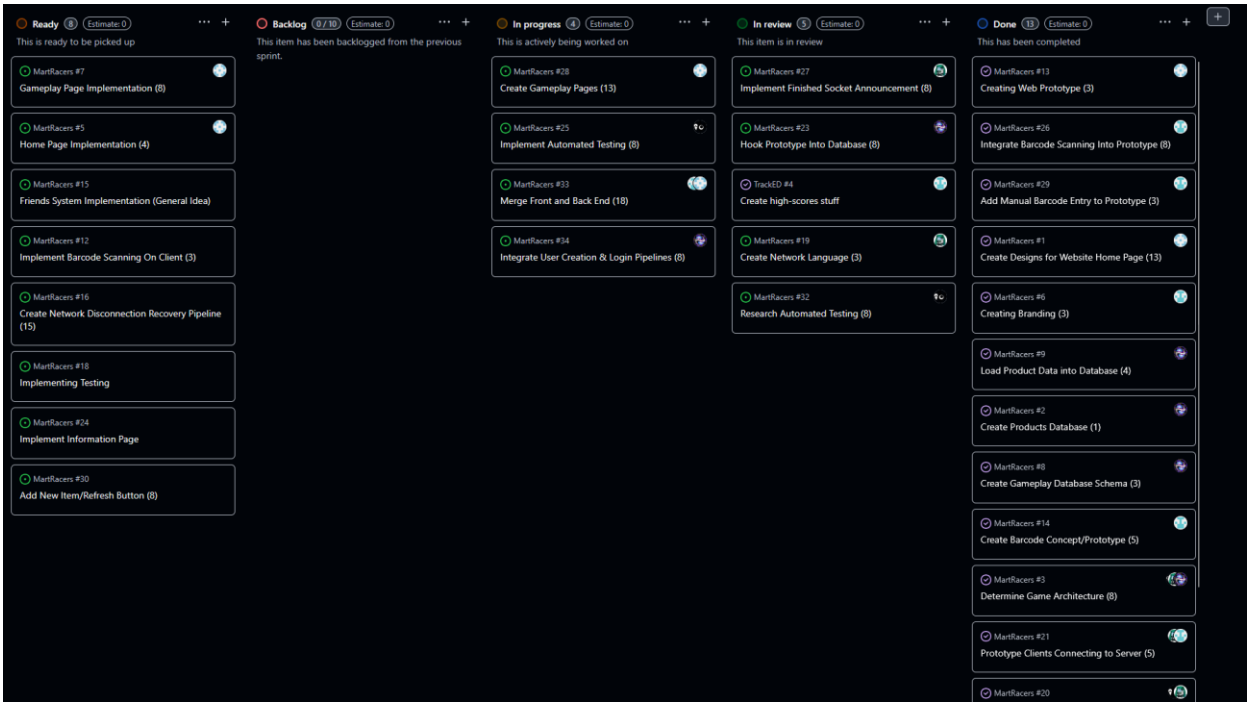

Many items remained in the “In Progress” column due to the larger scopes of work compared to the less output

Velocity

Only 8 story points were completed in full this week as most tasks were still considered as “In Progress.”

Attendance

All members were present for all three sprint meetings during this sprint.
